

www.citiesinspection.com

October 5, 2015

Dear Home Buyers,

On June 1, 2015, Cities' Inspection Service, Inc. completed a fourth stage new construction inspection of the property located at 123 Oak Street, Someplace Minnesota for you. Doug Hastings did all the fieldwork related to this project. Doug used the 2007 Minnesota State Building Code as the minimum construction standard.



The method used for this inspection was visual. There was no destructive analysis or technical testing of any building component. The project excluded all environmental health hazards, such as concealed mold, mildew and fungal growth; and any insect and vermin infestations.


The purpose of this inspection was to observe the construction of this home at various stages of completion. The intent of the inspection was to identify defects or conditions that adversely affect the integrity of the building. This report contains the results of the final inspection.

These definitions were used in this report:

- Meets component met or exceeded minimum industry standard and was consistent with the building plan and specification.
- Below component fell below minimum industry standard and/or was inconsistent with building plan and specification.
- Not complete component was not completed or was covered and not visible.

Final Inspection

Explanation of Problems

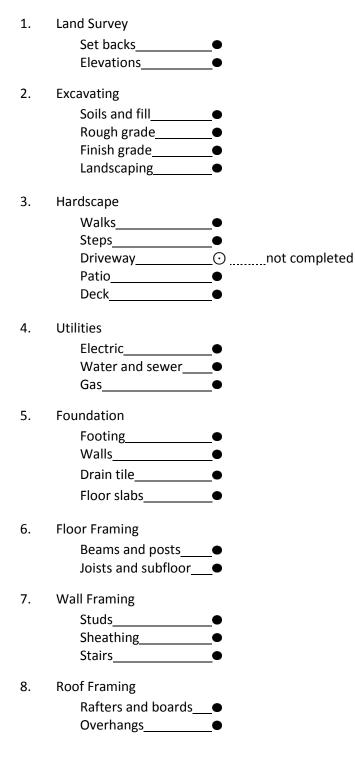

9. Wall Covering

9.	Wall Covering	
	Barriers and flashing_	
	Siding and trim●	
	Veneers●	
	Doors●	
	Windows⊗missing shutters	
10.	Roof Covering	
	ShinglesScaffolding left on root	f
	Flashing •	
	Gutters⊗sagged front gutter	
11.	Plumbing	
	Water supply●	
	Interior water pipes_	
	Water heater●	
	Waste pipes●	
	Drain and vent pipes_	
	Floor drain●	
	Kitchen fixtures●	
	Laundry fixtures●	
	Bath fixtures●	
	Bath rough in●	
	Distribution wiring●	
	Gas pipes●	
12.	Heating	
	Furnace●	
	Vent and flue●	
	Humidifier●	
	Air cleaner●	
	Ventilation●	
13.	Cooling	
	Condenser●	
	Refrigerant lines●	
	Wiring	
14.	Insulation	
	Foundation●	

Foundation•Rim Joist•Ground walls•Attic•Vaulted ceilings•Attic ventilation•Vapor retarders•

15. Millwork

Window trim●	
Baseboard trim●	
Interior doors●	
Garage doors●	
Stairs●	
Cabinets●	
Countertops●	
Finish hardwareO	no closet shelving / missing knobs & stops

16. Plastering

0	
Walls	•
Ceilings	•
Fire barriers	•

17. Flooring

-	
Underlayment	•
Wood floors	•
Tile floors	•
Carpet	•

18. Painting

Exterior	•
Interior walls	•
Interior trim	•
Cabinets	•

19. Glass Products

Mirrors	•
Shower doors	•
Bath accessories	•

20. Appliances

Kitchen	•	
Laundry	•	
Water softener	•	
Final cleaning	O	not completed

Conclusions and Recommendations

- 1. Major Defects
 - a. Sagged front gutter.
 - b. Scaffold jacks left on roof.
 - c. Missing garage window shutters.
 - d. Restricted opening of basement bar refrigerator door.

2. Potential Defects (Unfinished Work)

- a. Driveway
- b. Fence
- c. Closet shelving
- d. Finish hardware
- e. Interior cleaning
- 3. Final Comments

The general building construction exceeds the minimum industry building standard relative to material and workmanship. The attention to energy and moisture detail meets or in some instances exceeds today's building code standard.



1st inspection site



1st inspection foundation insulation



1st inspection soils



1st inspection backfill & wall bracing



1st inspection interior footings



2nd inspection building framing



2nd Inspection roofing




2nd inspection flashing



3rd inspection exterior barriers



3rd inspection caulking

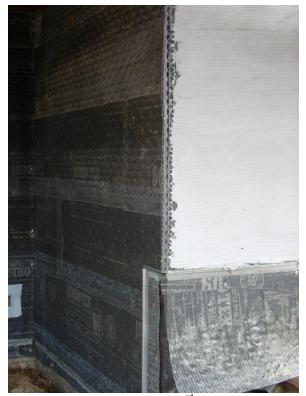

3rd inspection stucco







3rd inspection basement



3rd inspection insulation



3rd inspection insulation



3rd inspection insulation



3rd inspection vaulted ceilings



3rd inspection exposed nails



4th final inspection



4th final inspection
